


# STREETSCAPE BEAUTIFICATION

## COMPLETED – December 2011

**Medians:** South Murphy Road,  
Heritage Parkway and West Betsy Lane  
**Designer:** MESA Design Group – Dallas  
**Bid Award:** March 1, 2010  
**Construction Bid:** \$1,054,519.70  
(includes 1 year maintenance, expired  
12/31/2011)  
**Revised Contract:** \$1,056,418.26  
**Contractor:** American Landscape Systems  
**Completed Construction:** March 2011  
**December 13, 2010 City Council added  
median landscaping and entrance sign at  
West Betsy Lane and Parker City Limits.**

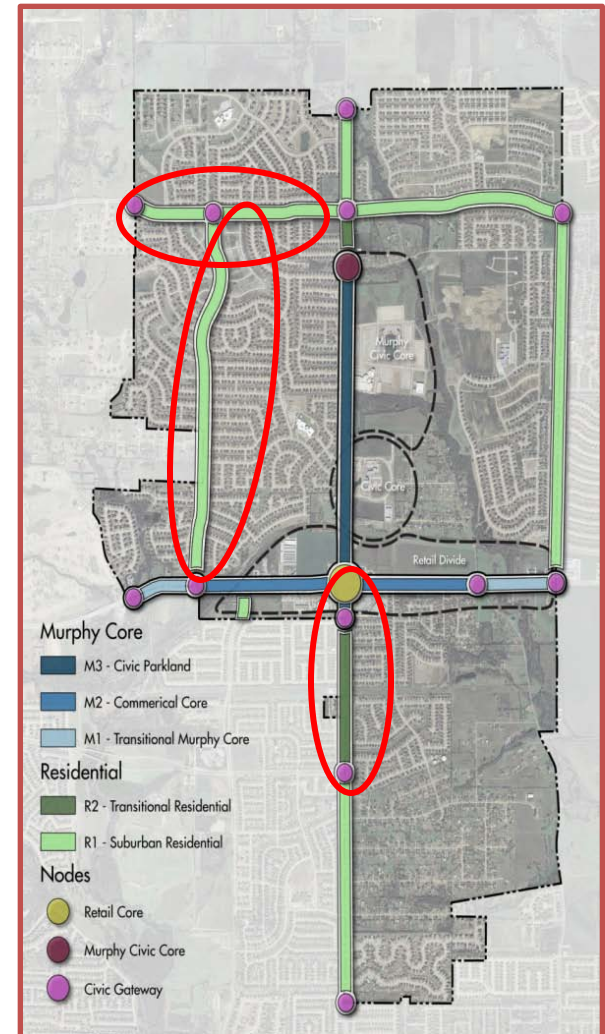

# STREETSCAPE BEAUTIFICATION

COMPLETED – December 2011




**Over 1,000 trees were planted on South Murphy Road, Heritage Parkway, and West Betsy Lane. All trees have drip / bubbler irrigation. Other grasses and plants selected were to be drought tolerant to reduce watering needs.**

# STREETSCAPE BEAUTIFICATION


## FM 544 – upgrade needed

FM 544 Redesign presented to Council December 6, 2010.  
FM 544 – Long Range Comprehensive Plan to be prepared and funded

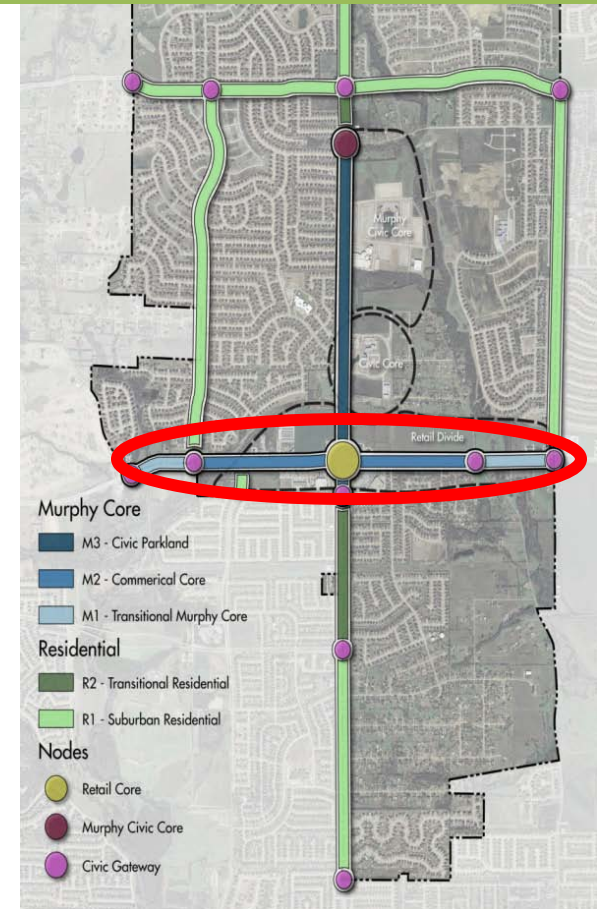

# STREETSCAPE BEAUTIFICATION

## FM 544 – upgrade master plan

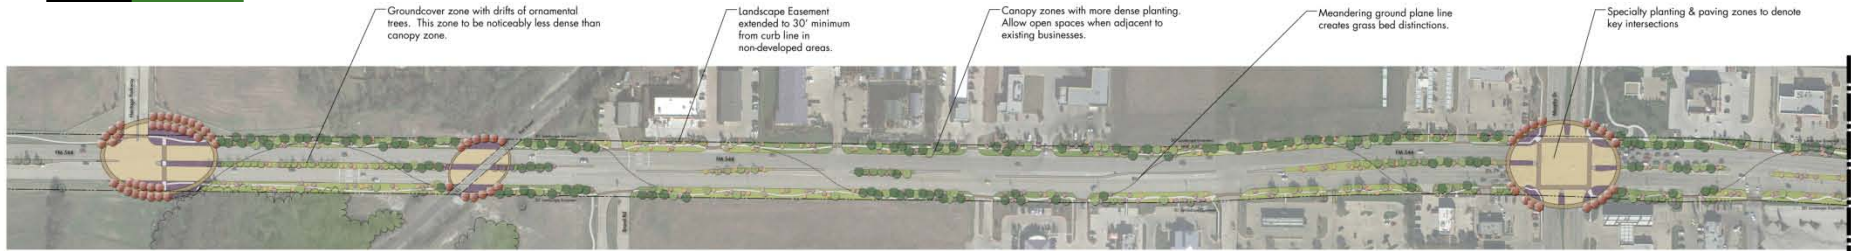

Streetscape Beautification - FM 544 Parkway  
Murphy, Texas

October 20, 2010 MESA

